



Northern Line Extension PROGRESS UPDATE

May 2020

NLE Kennington Park - restart

As you are aware, towards the end of March, we brought all our NLE construction sites to a 'Safe stop' in line with Transport for London coronavirus guidelines. We have since recstarted some activities at our Kennington Park site to allow works to resume safely. Additional precautionary measures are now in place.

Where we left off

Following the removal of the concrete foundation of the acoustic shed, the next phase in the sequence of works was to apply a waterproofing layer and concrete protective layer to the top of the basement structure. See the completed task in fig. 1 below. Brickwork on the head house commenced and the base level of bricks was installed.

Heading underground, the fit out teams were busy installing electrical and ventilation equipment, cable trays, ducting and doors to the rooms within the shaft corridors. (See fig. 2 below).



Fig. 1 Waterproofing the basement structure

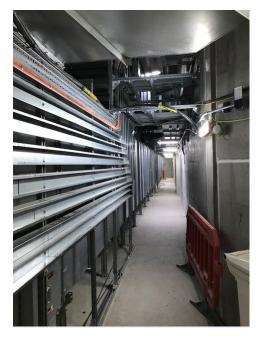


Fig.2 Installation of cabling trays within the shaft

At the start of May, we begun to implement some remobilisation measures to prepare the site for operatives to return to work safely. Materials were moved to create space for car parking facilities and walkways and social distance indication markers were put in place.





What is planned?

Over the coming months, we will resume works to install the brickwork façade to the head house. Below ground the mechanical and electrical teams will continue their work on the fit out within the shaft itself.

As we adapt to the new ways of working; avoiding the use of public transport where possible and with fewer people on site at any given time, we have adjusted the work schedule accordingly in order to maximise progress.

Please see below a revised timeline of activities to take place over the months ahead at the NLE Kennington Park site. You may notice some lower impact activities taking place on the surface until 21:00 Monday — Friday with works continuing underground through the night. Core hours remain on Saturday will remain as 08:00-13:00.

Activity	Start Date	End Date
Kennington Park Headhouse - Brickwork Facade	February 2020	August 2020
Mechanical & Electrical Installation of equipment inside the headhouse structure	Autumn 2019	Autumn 2020
Removal of concrete hardstanding from Kennington Park site, landscaping works and reinstatement of new roads and paving.	Autumn 2020	Winter 2020
Removal of main hoarding – access to the headhouse area will be required until 2021. Park will remain fenced off.	Spring 2020	Autumn 2020
Tree planting	Winter 2020	Spring 2021

Please note that all above-mentioned works will be carried out diligently while adhering to coronavirus requirements and guidelines around social distancing. This notification is being communicated to the local authority.

The Northern line extension helpline remains open 24/7. Please do get in touch via the contact details below should you have any queries or questions.

We hope you and your loved ones stay safe and well.
